
Neumann Residence - 1567 Steveles Crescent, Mississauga - Construction Schedule

Chatsworth Fine Homes | Status date Oct 13, 2026 | Page 1 of 4

Preconstruction, Design & Approvals		
CVC Permit 26/255 issued (expires Oct 2, 2028)	Darren (Structured Creat	Oct 02
Zoning review - City of Mississauga	Darren (Structured Creat	
Correct A100 coverage table and CVC permit owner name	Darren / Gosia	
Working drawings - architectural & structural (incl. basement program)	Darren (Structured Creat	
Building permit application submitted	Darren / Andrew	Oct 29
City permit review incl. one comment cycle (assumed 25 working days)	City of Mississauga	
Building permit issued	City of Mississauga	Dec 03
Budget Revision 4 - anchor budget to current scope (incl. loft / 3rd f	Dan / Gosia	
Interior design drawings & ID budget (Vicky)	Vicky (ID) / Gosia	
Net Zero palette - incremental pricing by item	Gosia / Building Knowled	
Client decision - Net Zero direction, fireplace, window spec	Stephen (Owner)	
Price basement slab insulation options A / B incl. height loss	Gosia	
Client decision - basement slab option	Stephen (Owner)	
Underground hydro service - pricing from City / Alectra	Gosia	
Client decision - underground hydro service	Stephen (Owner)	
Generator sizing, pricing & client decision	Dan / Stephen	
Confirm builder's risk / wrap-up insurance & issue PO	David	
Tendering, Trade Awards & Long-Lead Procurement		
Award demolition (recommend Manpower - $49,025 incl. asbestos & loft)	Andrew / Dan	
PO site hoarding, fence & silt control	David	
Book Alectra overhead disconnect & temp pole	Gosia	
Excavation quotes - Kruno / Grizzly; all-in-one vs. separate	Gosia	
Award excavation, foundation & underpinning (recommend EECF)	Dan / Gosia	
Tender & award framing labour (RamPeel, King, Murray, Sunvalley, VAV)	Gosia	
PO lumber & roof framing; delivery	Gosia	
Steel beams - confirm scope, shop drawings, fabricate	Dan	
Measure brick openings; issue window / mill schedule	Andrew / Stephen	
Window tender - double vs. triple pane, heritage profile	Andrew	
Window, exterior door & skylight PO	Andrew / Stephen	
Window, door & skylight fabrication & delivery (~10 wks)	Supplier	
HVAC design / heat loss - heat pump, HRV/ERV per Net Zero direction	Dan / Andrew / Gosia	
Award HVAC / mechanical	Gosia	
Award plumbing	Gosia	
Award electrical (confirm EV charging, solar & AV scope)	Gosia	
Award insulation & drywall	Gosia	
Award finishing trades - tile, flooring, trim, paint	Gosia	
Kitchen & cabinetry design approval	Vicky (ID) / Stephen	
Cabinetry shop drawings & sign-off	Cabinetmaker / Vicky	
Cabinetry fabrication	Cabinetmaker	
Interior stair & railing shop drawings & fabrication	Stair supplier	
Owner & Interior Design Selections		
Electrical, lighting & AV / automation layouts	Vicky / Stephen	
Plumbing fixtures & bathroom layouts (curbless showers ensuite 1 & 2)	Vicky / Stephen	
Fireplace / logsets & mantels	Stephen	
Exterior - cedar shake, metal panel, colours, railings, garage door	Stephen / Darren	
Hardwood, floor tile & wall tile	Vicky / Stephen	
Trim, interior doors, plaster mouldings, hardware	Vicky / Stephen	

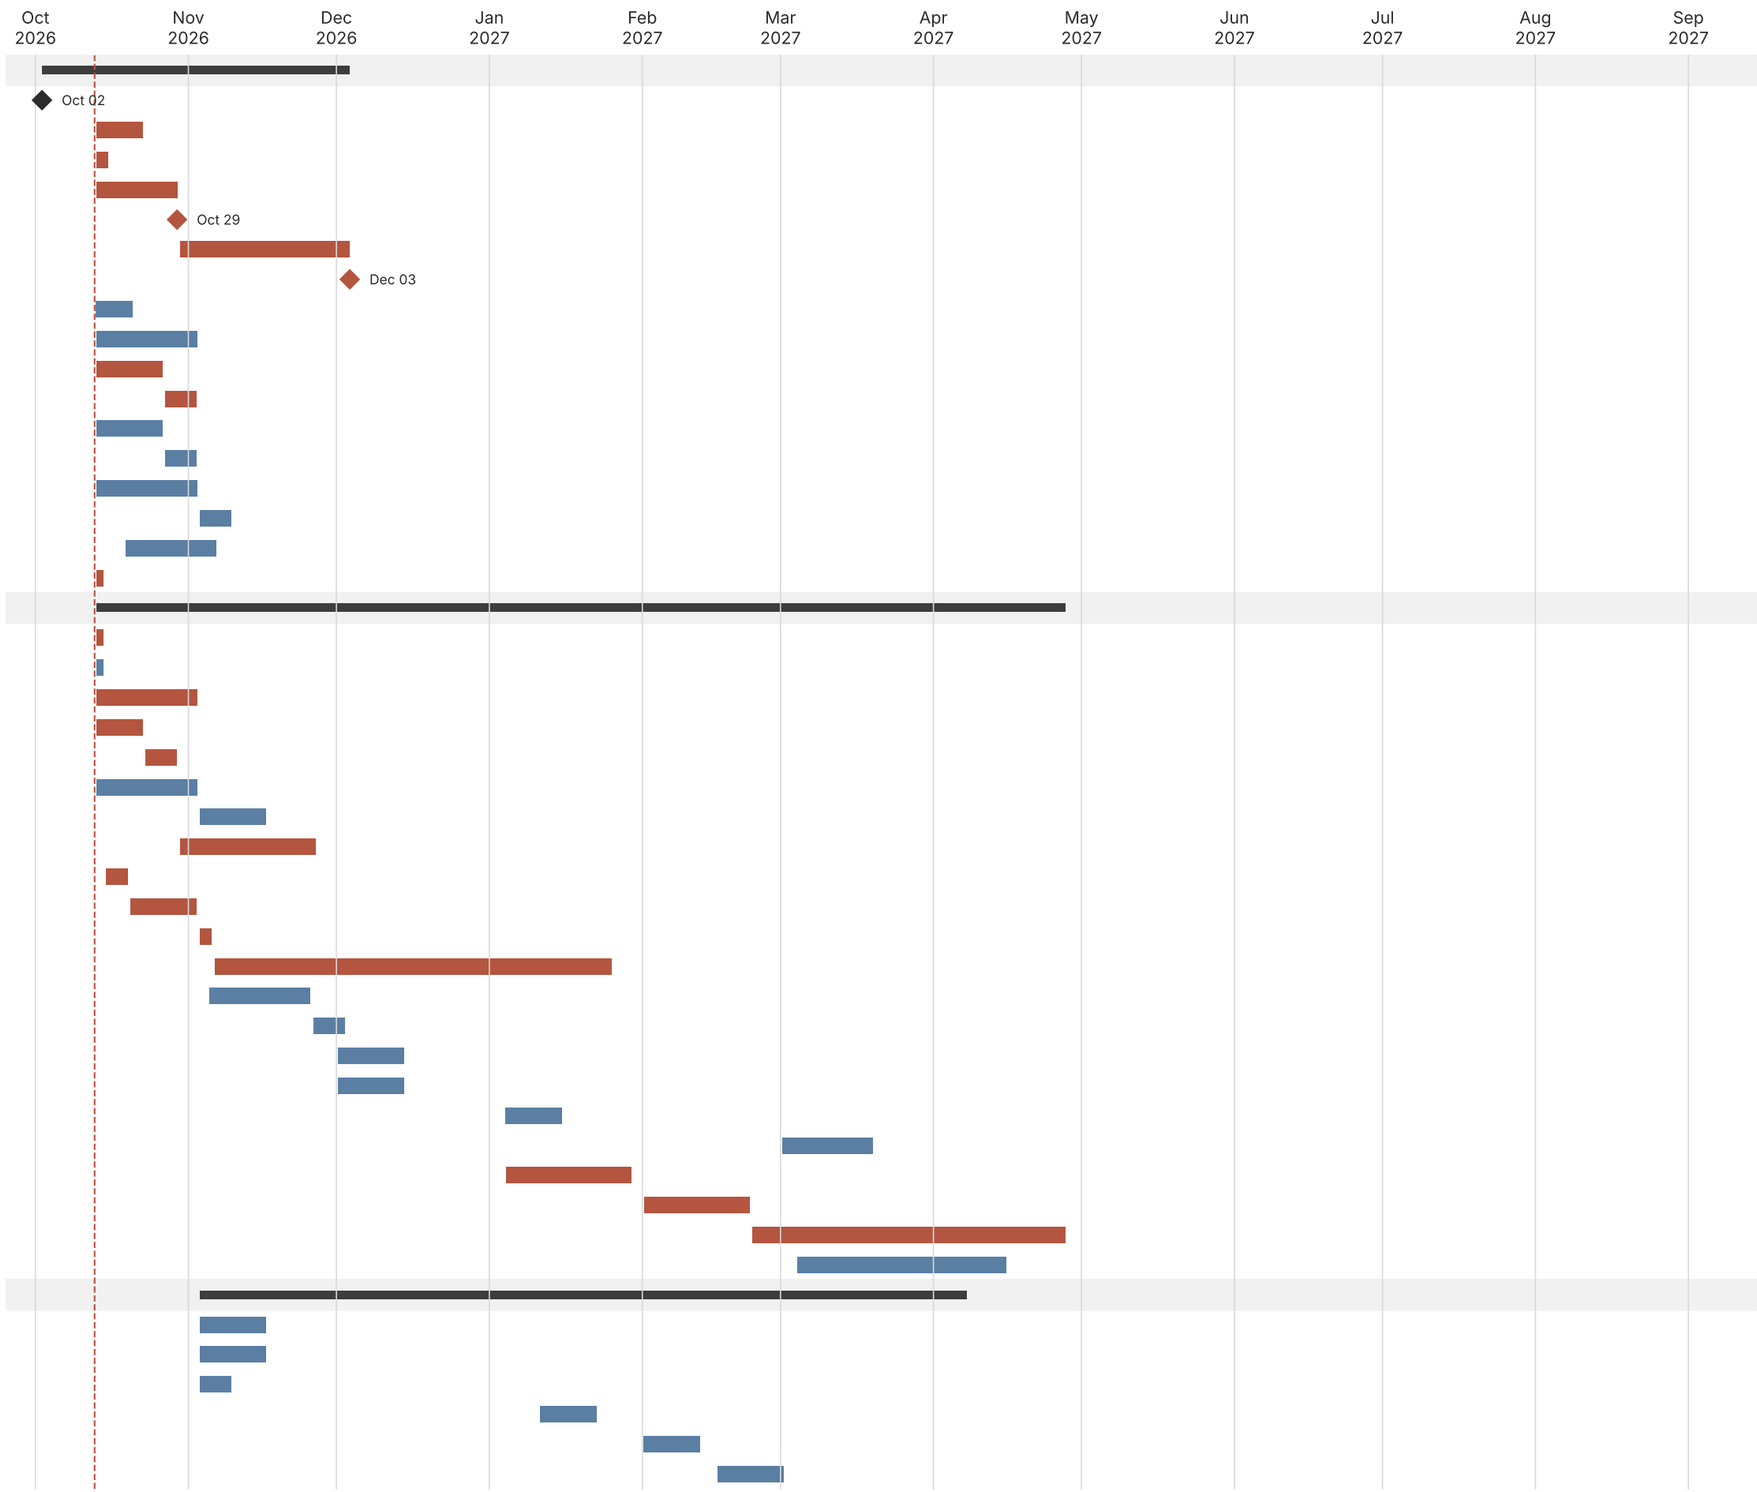


Blue: task Red: critical path Green: complete Diamond: milestone Red triangle: target date Dashed line: status date

Neumann Residence - 1567 Steveles Crescent, Mississauga - Construction Schedule

Chatsworth Fine Homes | Status date Oct 13, 2026 | Page 2 of 4

Appliances	Stephen
Countertop slabs, shower glass & bath hardware	Vicky / Stephen
Paint finish schedule	Vicky / Stephen
Site Mobilization & Pre-Demolition	
Site possession - family moved out (confirm Oct 15)	Stephen (Owner)
Building Knowledge as-is audit & baseline air test	Andrew / Building Knowle
Pre-demolition condition photos (HST rebate documentation)	Andrew / Stephen
Designated substance / hazardous materials confirmation	Andrew
Job site sign & Notice of Project posted	Dillon
Site fencing, tree protection & erosion / sediment controls	Site super
Temp facilities - porta potty, bins, security, internet	Site super
Remove, label & store salvage items	Site super
Interior Demolition (non-structural, pre-permit)	
Asbestos abatement - 2nd floor SW & SE bedroom ceilings	Demo trade
Strip-out - loft / 3rd floor	Demo trade
Strip-out - second floor	Demo trade
Strip-out - main floor	Demo trade
Strip-out - basement	Demo trade
HVAC designer as-is walk (ducting exposed)	Andrew
Assess existing rough-ins - keep / replace decisions	Dan / Andrew / trades
Interior demolition complete	
Utilities & Temporary Services	
Disconnect overhead service; temp pole & panel	Electrician / Alectra
Permanent hydro service (underground if approved)	Alectra / Electrician
Gas service remove & reinstall as required (Enbridge)	Gas fitter
Site Work, Excavation & Foundations (rear addition)	
CVC 48-hr notice of commencement; permit card posted	Andrew
Survey stake-out of addition	Surveyor
Structural demo - rear deck / porch, openings, 2nd-floor bump-out wall	Demo trade
Strip & stockpile topsoil	Excavator
Excavate rear addition	Excavator
Underpinning - 8 sections, sequenced	Foundation trade
Layout, pin & form footings	Foundation trade
Footing inspection	City inspector
Pour footings (winter heat)	Foundation trade
Form foundation walls & install rebar	Foundation trade
Engineer's rebar inspection	Structural engineer
Pour foundation walls	Foundation trade
Strip forms; check heights & anchor bolts	Foundation trade
Membrane, 2" exterior insulation, weepers, stone & sump	Foundation trade
Foundation as-built survey	Surveyor
Backfill inspection	City inspector
Backfill & rough grade	Excavator
Framing & Structure	
Interior structural alterations - openings, beams, bulkheads	Framer
Install steel beams / posts	Framer / welder
Frame main floor deck - rear addition	Framer
Frame addition walls & flat roof	Framer

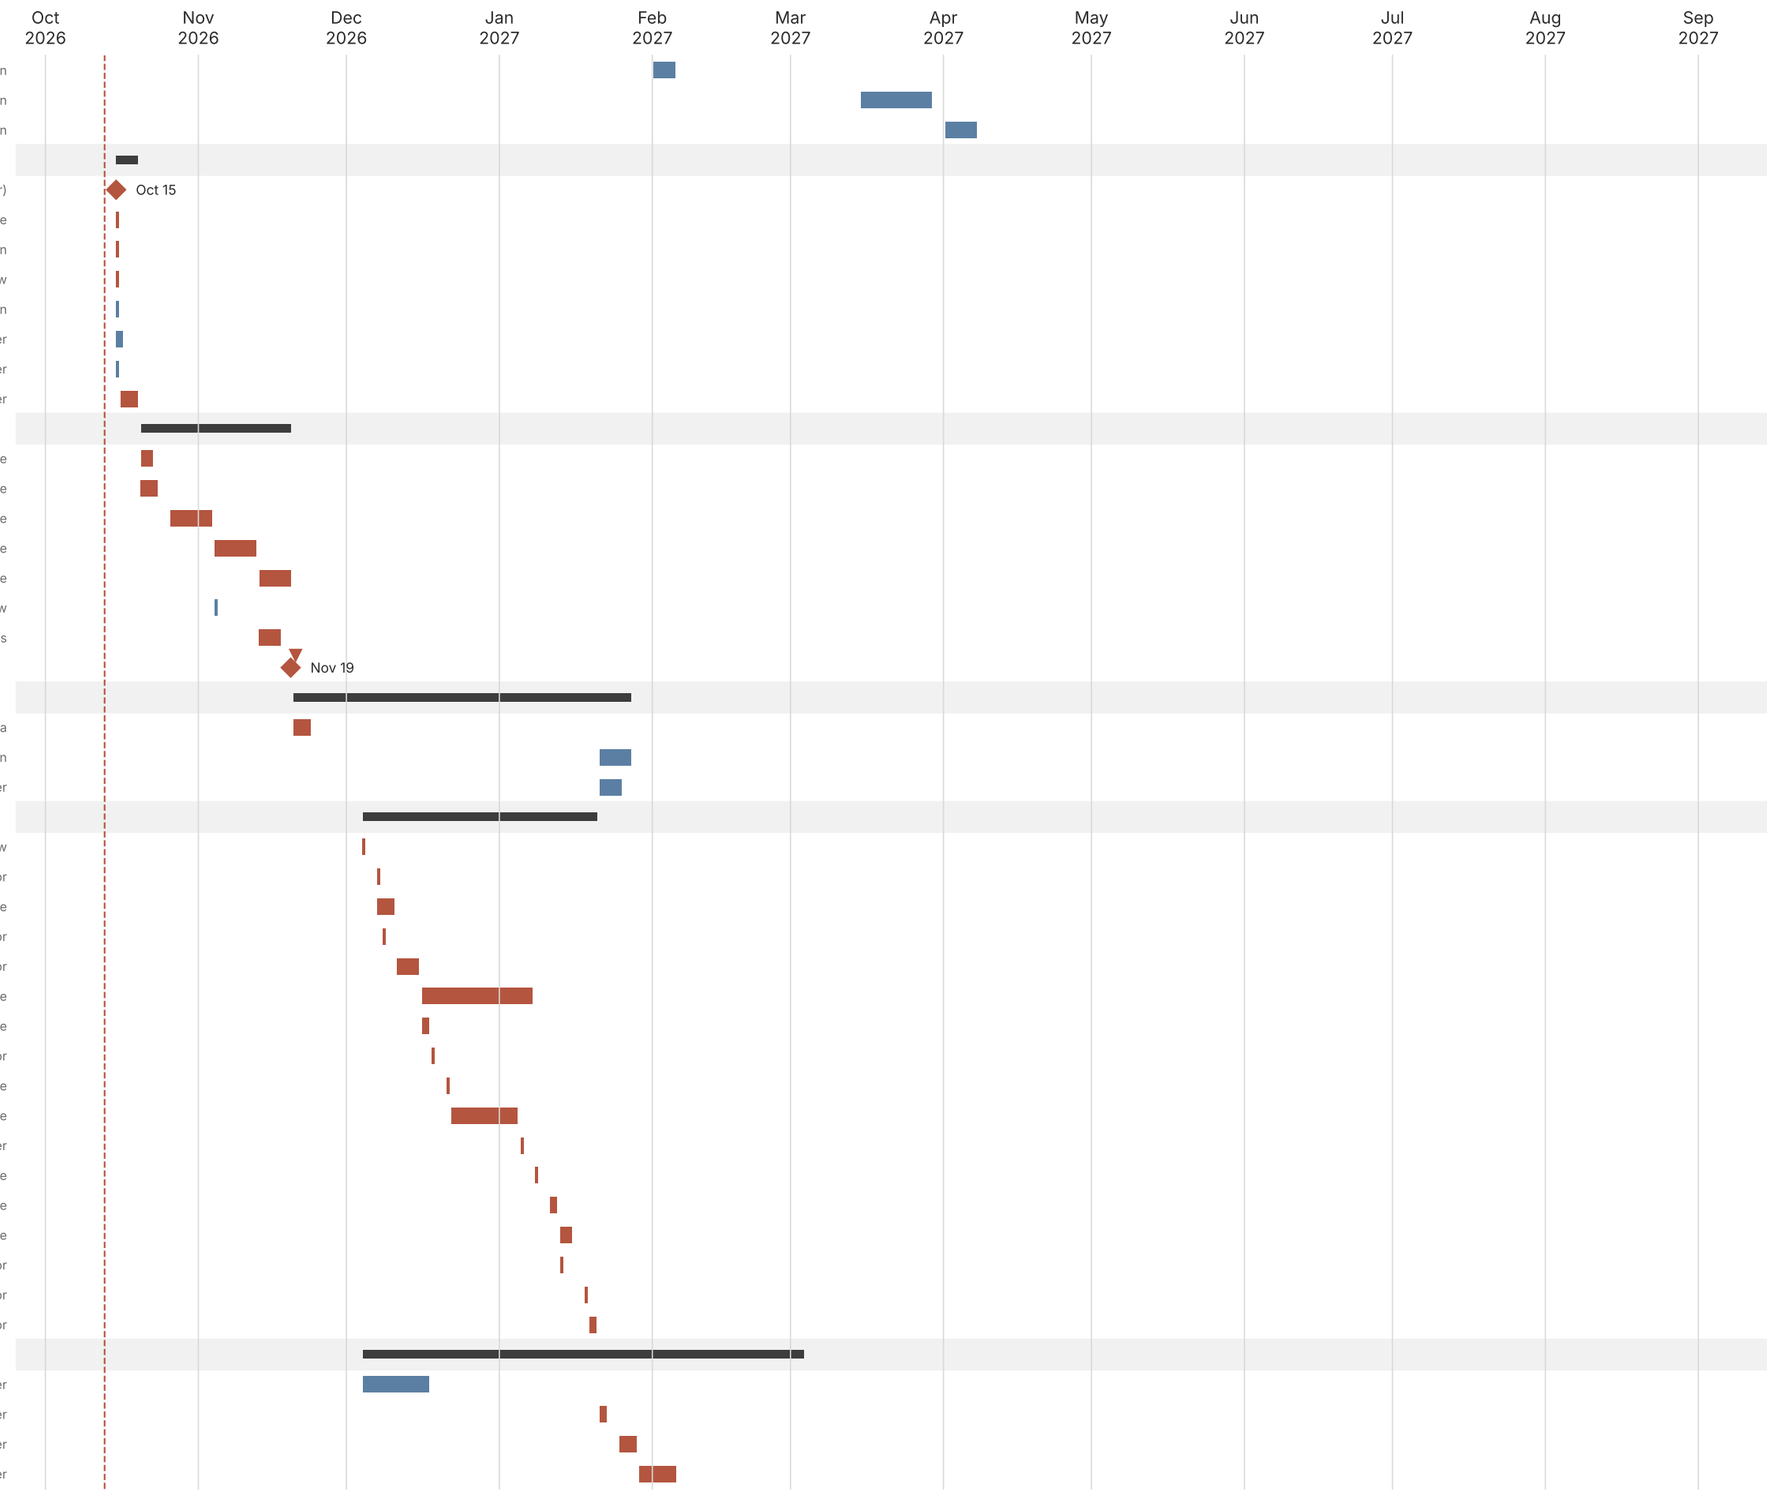


Blue: task Red: critical path Green: complete Diamond: milestone Red triangle: target date Dashed line: status date

Neumann Residence - 1567 Steveles Crescent, Mississauga - Construction Schedule

Chatsworth Fine Homes | Status date Oct 13, 2026 | Page 3 of 4

Cantilevered box bays, 2nd-floor infill & balcony	Framer
Roof & wall sheathing; Zip-R outsulation	Framer
Framing review - point loads, engineer review, deficiencies	Framer / engineer
Building Envelope - Weathertight	
Temporary enclosure, tarping & winter heat	Site super
Flat roof membrane & flashings (addition, balcony)	Roofer
Shingle roof tie-ins & repairs	Roofer
Replace designated windows & doors in existing openings	Window installer
Install windows & doors - rear addition & box bays	Window installer
Install architectural skylight	Roofer
Watertight	
Basement Slab & Underground Services	
Subgrade drains & underground plumbing	Plumber
Underground drain inspection	City inspector
Under-slab insulation, radon / vapour barrier	Concrete trade
In-floor hydronic tubing (if carried in mechanical design)	Mechanical
Pour basement slab	Concrete trade
Mechanical, Electrical & Low-Voltage Rough-In	
Rough-in plumbing - existing house	Plumber
Rough-in HVAC - duct rework, heat pump / HRV-ERV - existing house	HVAC
Rough-in gas - fireplace, range, BBQ manifold	Gas fitter
Rough-in electrical incl. EV charger & solar conduit - existing house	Electrician
Rough-in low voltage - data, security, AV, intercom reinstatement	LV contractor
Rough-in walkthrough with client & ID; changes	Andrew / Stephen / Vicky
Rough-in inspections - existing house (plumbing, HVAC, framing, ESA)	City / ESA
Rough-in inspections passed - existing house	
Rough-in all trades - rear addition & box bays	All MEP trades
Rough-in inspections - rear addition	City / ESA
Insulation, Air Sealing & Drywall	
AeroSeal duct sealing (reused ductwork)	HVAC
Insulation & VB - existing house, sound insulation	Insulation trade
Insulation & VB - addition, ceiling spray foam	Insulation trade
Insulation / VB inspection	City inspector
Mid-construction blower door test	Building Knowledge
Board drywall	Drywall trade
Tape & finish drywall	Drywall trade
Prime drywall (tinted)	Painter
Plaster mouldings	Plaster trade
Interior environment controlled (permanent HVAC running)	HVAC
Interior Finishes	
Floor tile & Schluter waterproofing	Tile setter
Hardwood & LVP	Flooring trade
Install interior stairs & railings	Stair supplier
Doors, trim, panelling, closets & shelving	Trim carpenter
Install cabinetry - kitchen, island, servery, vanities, laundry	Cabinetmaker
Template, fabricate & install countertops	Countertop fabricator
Wall tile, showers & backsplashes	Tile setter
Interior painting	Painter

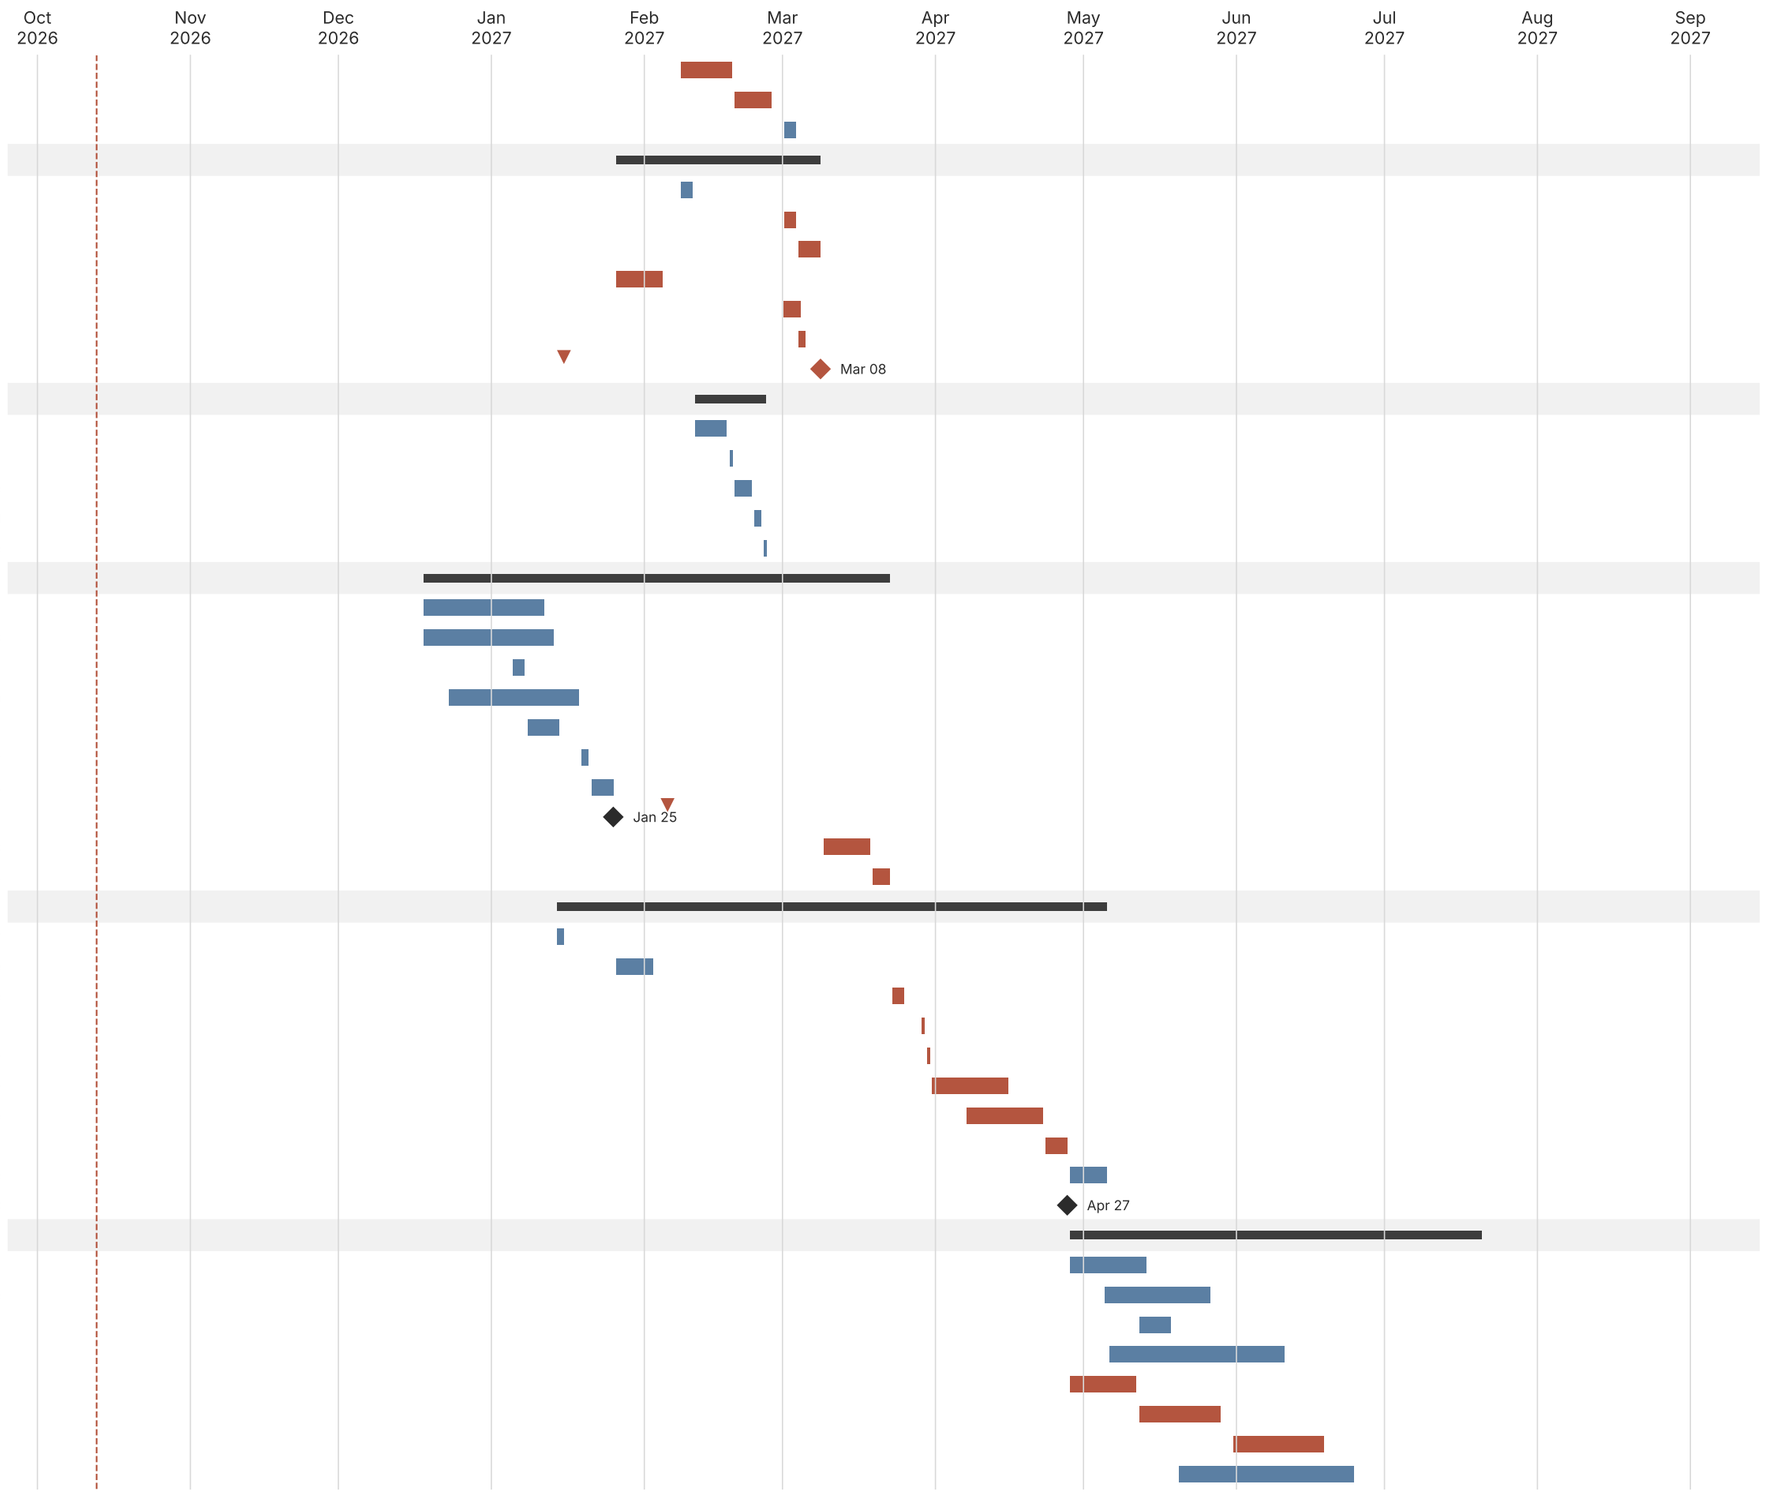


Blue: task Red: critical path Green: complete Diamond: milestone Red triangle: target date Dashed line: status date

Neumann Residence - 1567 Steveles Crescent, Mississauga - Construction Schedule

Chatsworth Fine Homes | Status date Oct 13, 2026 | Page 4 of 4

Reinstall salvaged items; fireplace brick cladding & mantel	Trim carpenter / mason
Shower glass - template, fabricate, install	Glass supplier
Appliances delivery & install	Appliance supplier
Plumbing finishing - fixtures	Plumber
Electrical finishing - devices, pot lights, fixtures	Electrician
HVAC finishing - grilles, humidifier, HRV balancing	HVAC
Door hardware, bath accessories, mirrors	Trim carpenter
Sand & finish hardwood; stain stairs	Flooring trade
Final trade & paint touch-ups	All trades
Exterior Finishes & Landscaping	
Cedar shake siding	Siding trade
Exterior trim, columns, fascia & soffits	Exterior carpenter
Masonry repointing & flagstone front porch	Mason
Porch ceilings - cedar T&G	Exterior carpenter
Eavestroughs & downspouts	Eavestrough trade
Solar PV (required for Net Zero - not in budget)	Solar contractor
Rear deck (Trex), balcony & exterior railings	Deck builder
Exterior painting & caulking	Painter
Garage door	Garage door supplier
Hard landscaping - interlock, walls, fences	Landscaper
Soft landscaping & restoration of disturbed areas	Landscaper
CVC notice of completion	Andrew
Commissioning, Inspections & Handover	
Final blower door & EnerGuide / Net Zero labelling test	Building Knowledge
Duct cleaning	Duct cleaner
Final building inspection	City inspector
Final cleaning, windows & power wash	Cleaners
Client walkthrough & deficiency list	Andrew / Stephen
Occupancy / substantial completion	
Client move-in	Stephen (Owner)
Deficiency completion	All trades

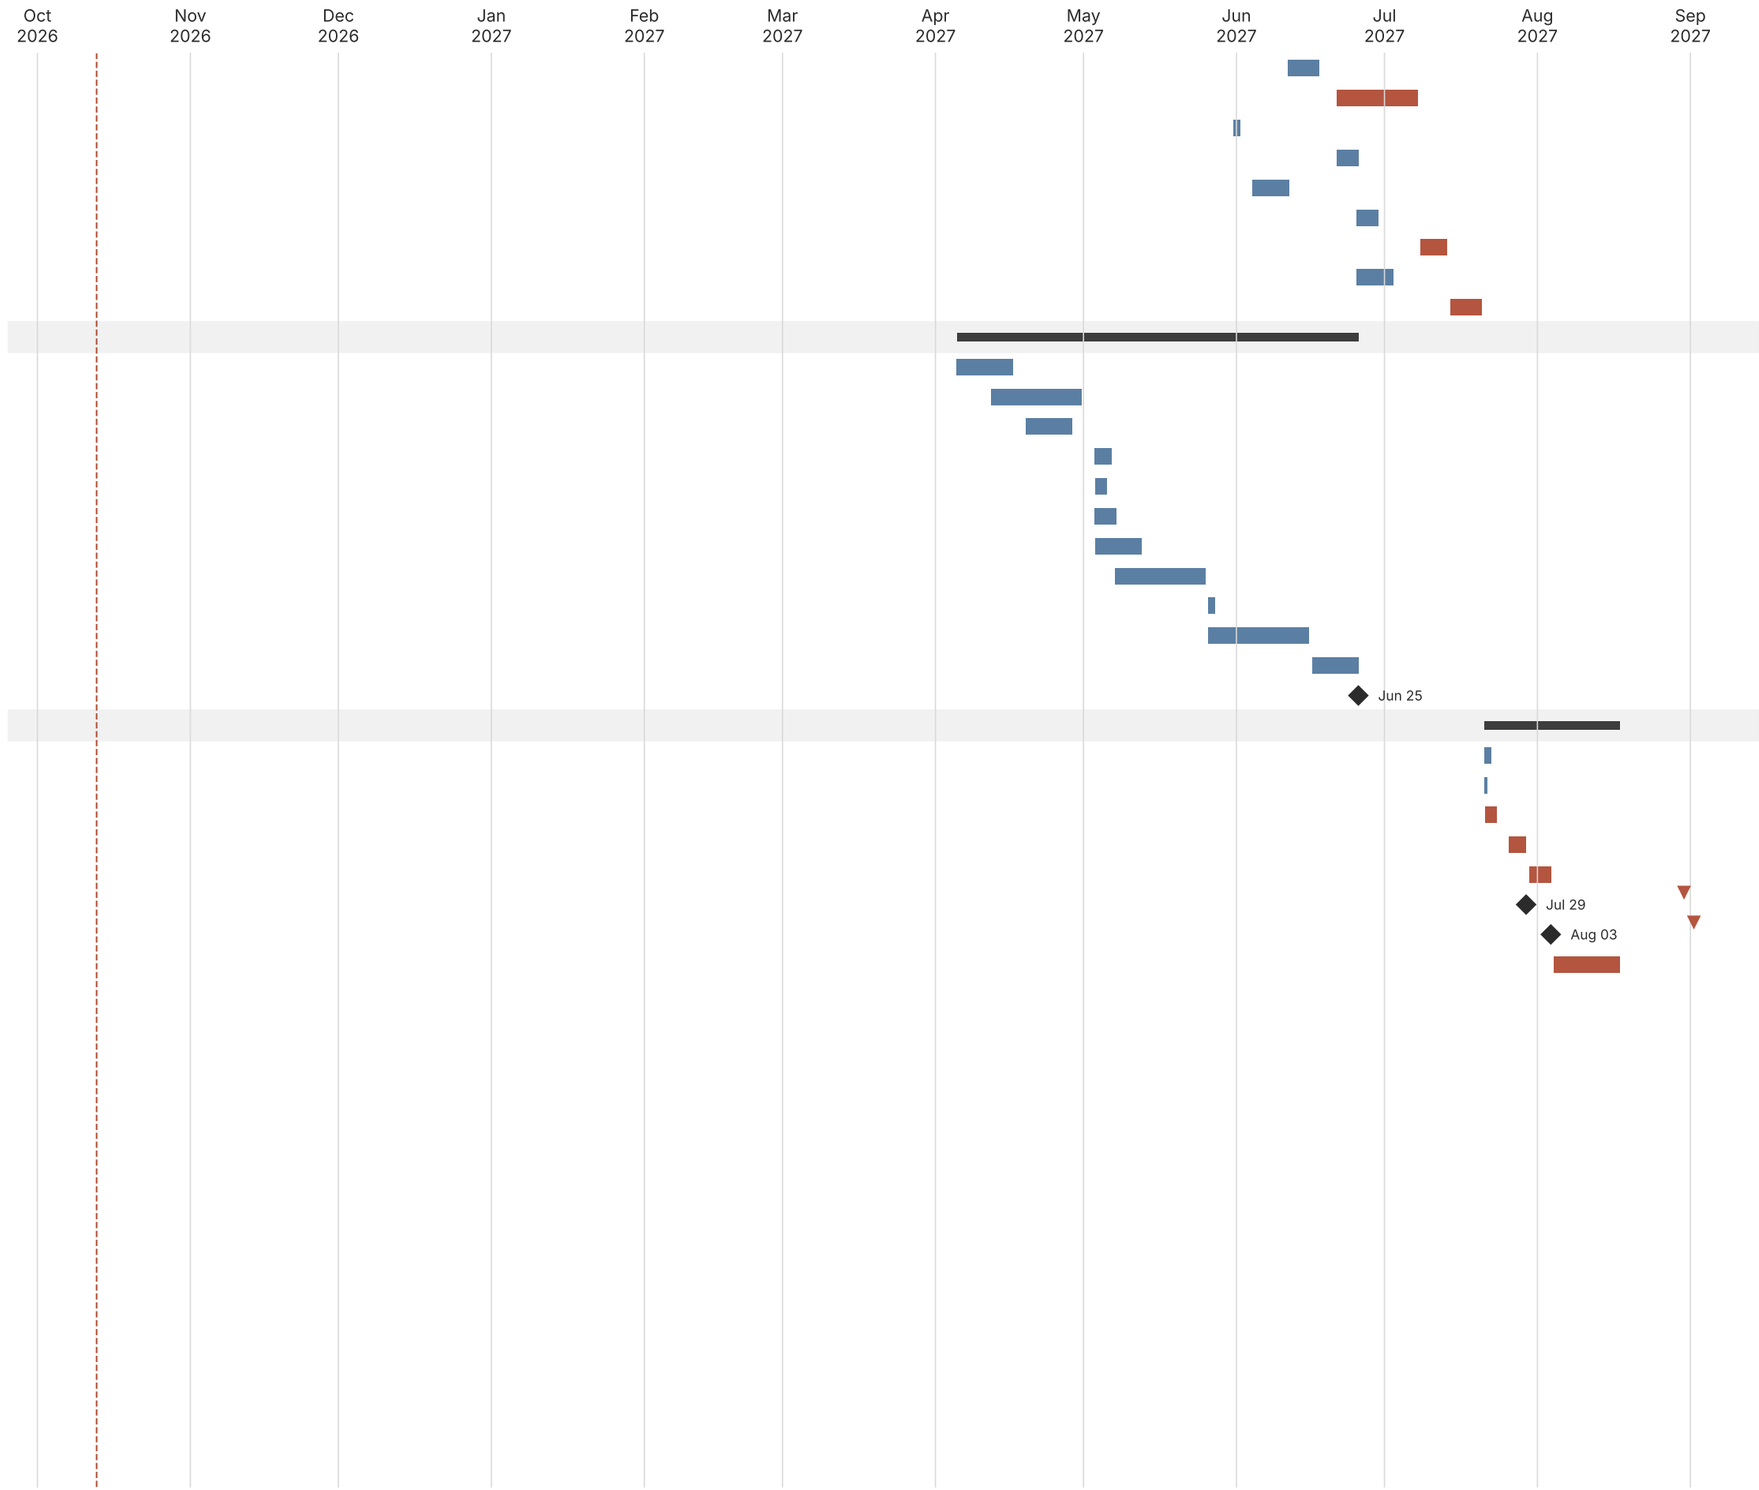

Blue: task Red: critical path Green: complete Diamond: milestone Red triangle: target date Dashed line: status date
